


Id	Task Name	Duración	Comienzo	Fin	Predecesoras	2 ene '00							9 ene '00							16 ene '00							23 ene '00							30 ene '00							6 feb '00							13 feb '00							20 feb '00
						S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D						
1	Software Development	89,5 días	lun 3/01/00	vie 5/05/00																																																			
2	Design	14,5 días	lun 3/01/00	vie 21/01/00																																																			
3	Review preliminary software specifications	2 días	lun 3/01/00	mar 4/01/00																																																			
4	Develop functional specifications	5 días	mié 5/01/00	mar 11/01/00	3																																																		
5	Develop prototype based on functional specifications	4 días	mié 12/01/00	lun 17/01/00	4																																																		
6	Review functional specifications	2 días	mar 18/01/00	mié 19/01/00	5																																																		
7	Incorporate feedback into functional specifications	1 día	jue 20/01/00	jue 20/01/00	6																																																		
8	Obtain approval to proceed	4 hrs	vie 21/01/00	vie 21/01/00	7																																																		
9	Design complete	0 días	vie 21/01/00	vie 21/01/00	8																																																		
10	Development	33 días	vie 21/01/00	mié 8/03/00																																																			
11	Review functional specifications	1 día	vie 21/01/00	lun 24/01/00	9																																																		
12	Identify modular/tiered design parameters	1 día	lun 24/01/00	mar 25/01/00	11																																																		
13	Assign development staff	1 día	mar 25/01/00	mié 26/01/00	12																																																		
14	Develop code	15 días	mié 26/01/00	mié 16/02/00	13																																																		
15	Developer testing (primary debugging)	15 días	mié 16/02/00	mié 8/03/00	14																																																		
16	Development complete	0 días	mié 8/03/00	mié 8/03/00	15																																																		
17	Testing	4 días	vie 21/01/00	jue 27/01/00																																																			
18	Develop unit test plans using product specifications	4 días	vie 21/01/00	jue 27/01/00	9																																																		
19	Develop integration test plans using product	4 días	vie 21/01/00	jue 27/01/00	9																																																		
20	Unit Testing	15 días	mié 8/03/00	mié 29/03/00																																																			
21	Review modular code	5 días	mié 8/03/00	mié 15/03/00	18;16																																																		
22	Test component modules to product specifications	2 días	mié 15/03/00	vie 17/03/00	16;21																																																		
23	Identify anomalies to product specifications	3 días	vie 17/03/00	mié 22/03/00	22																																																		
24	Modify code	3 días	mié 22/03/00	lun 27/03/00	23																																																		
25	Re-test modified code	2 días	lun 27/03/00	mié 29/03/00	24																																																		
26	Unit testing complete	0 días	mié 29/03/00	mié 29/03/00	25																																																		
27	Integration Testing	12 días	mié 29/03/00	vie 14/04/00																																																			
28	Test module integration	5 días	mié 29/03/00	mié 5/04/00	26																																																		
29	Identify anomalies to specifications	2 días	mié 5/04/00	vie 7/04/00	28																																																		
30	Modify code	3 días	vie 7/04/00	mié 12/04/00	29																																																		
31	Re-test modified code	2 días	mié 12/04/00	vie 14/04/00	30																																																		
32	Integration testing complete	0 días	vie 14/04/00	vie 14/04/00	31																																																		
33	Training	57 días	vie 21/01/00	mar 11/04/00																																																			
34	Develop training specifications for end users	3 días	vie 21/01/00	mié 26/01/00	9																																																		
35	Develop training specifications for helpdesk	3 días	vie 21/01/00	mié 26/01/00	9																																																		
36	Identify training delivery methodology (computer based training, classroom,	2 días	vie 21/01/00	mar 25/01/00	9																																																		
37	Develop training materials	3 sem.	mié 8/03/00	mié 29/03/00	34;16;35;36																																																		
38	Conduct training usability study	4 días	mié 29/03/00	mar 4/04/00	37																																																		

Project: Software Development Date: jue 23/01/25	Task		External Tasks		Inactive Summary		Start-only		Deadline	
	Split		External Milestone		Manual Task		Finish-only			
	Milestone		Inactive Task		Duration-only		External Tasks			
	Summary		Inactive Milestone		Manual Summary Rollup		External Milestone			
	Project Summary		Inactive Milestone		Manual Summary		Progress			

[illegible]

Project: Software Development Date: jue 23/01/25	Task		External Tasks		Inactive Summary		Start-only		Deadline	
	Split		External Milestone		Manual Task		Finish-only			
	Milestone		Inactive Task		Duration-only		External Tasks			
	Summary		Inactive Milestone		Manual Summary Rollup		External Milestone			
	Project Summary		Inactive Milestone		Manual Summary		Progress			

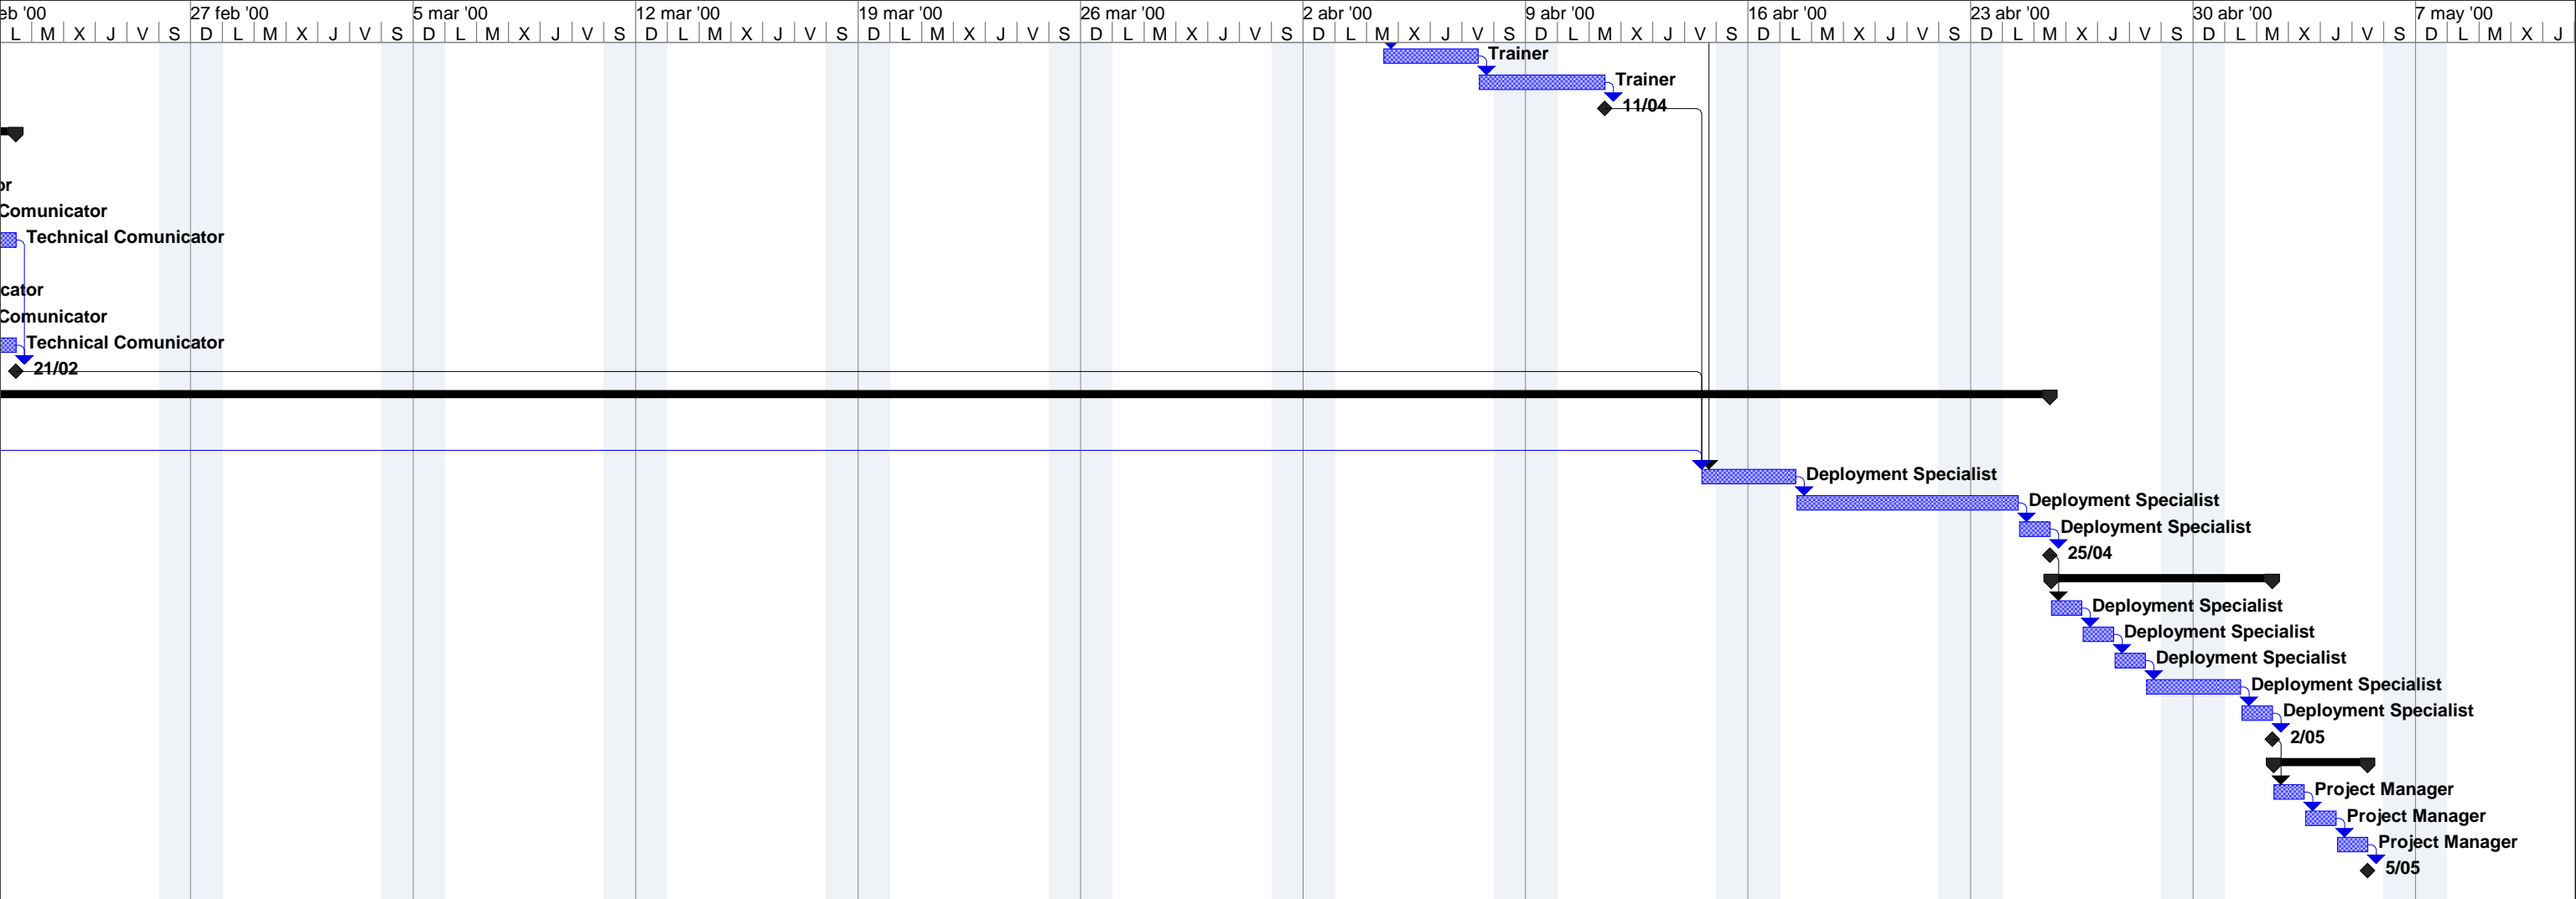

Project: Software Development Date: jue 23/01/25	Task		External Tasks		Inactive Summary		Start-only		Deadline	
	Split		External Milestone		Manual Task		Finish-only			
	Milestone		Inactive Task		Duration-only		External Tasks			
	Summary		Inactive Milestone		Manual Summary Rollup		External Milestone			
	Project Summary		Inactive Milestone		Manual Summary		Progress			
